


For additional information on any Capital Improvement Project, please contact the Town of Prosper Engineering Department at (972) 346-3502 or engineer@prospertx.gov.

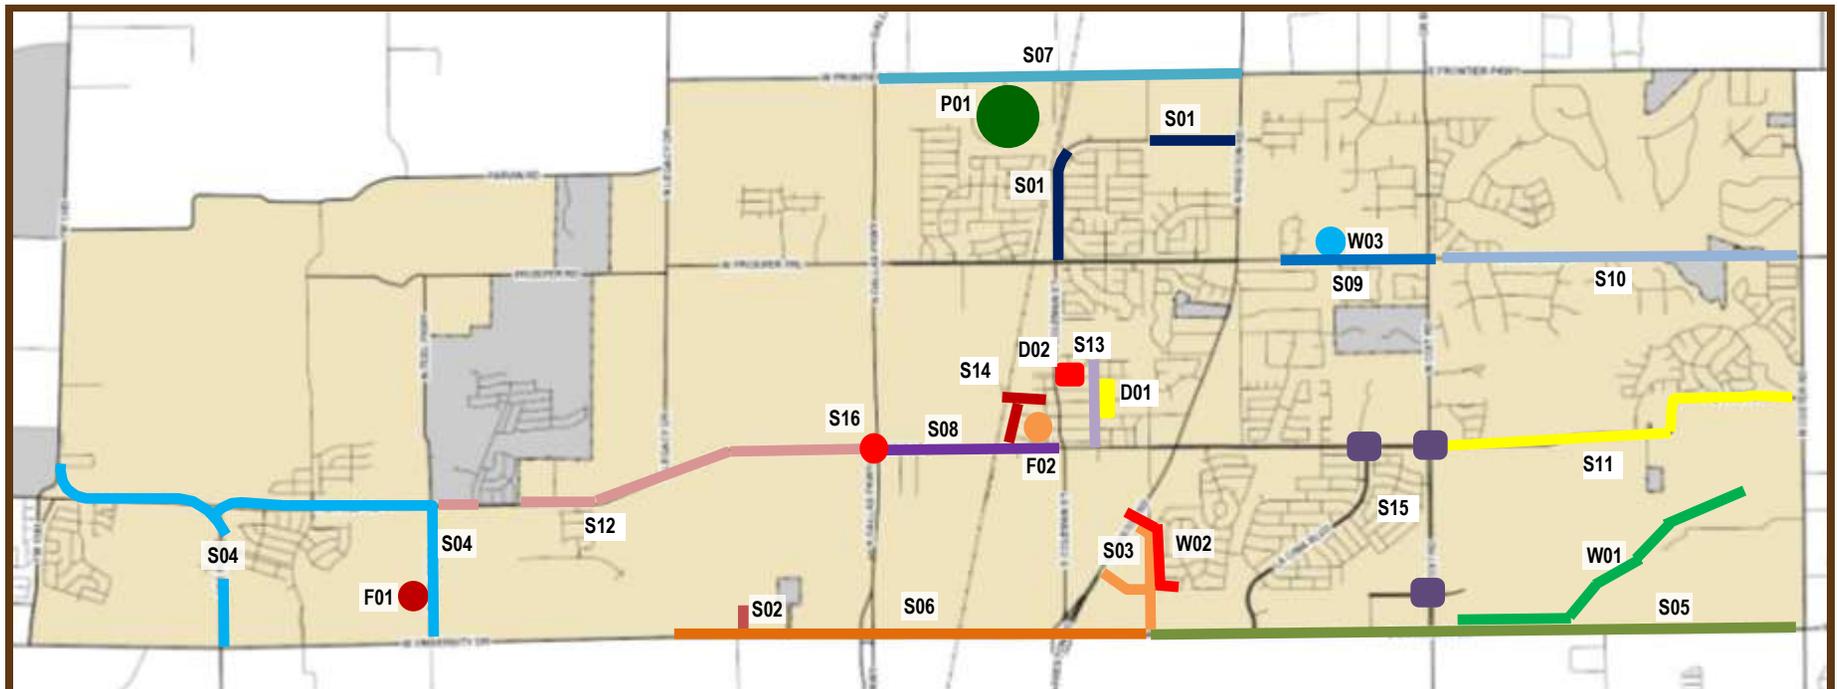

DISCLAIMER: The Town of Prosper has prepared this map or information for internal use only. It is made available under the Public Information Act. Any reliance on this map or information is AT YOUR OWN RISK. Prosper assumes no liability for any errors, omissions, or inaccuracies in the map or information regardless of the cause of such or for any decision made, action taken, or action not taken in reliance upon any maps or information provided herein. Prosper makes no warranty, representation, or guarantee of any kind regarding any maps or information provided herein or the sources of such maps or information and **DISCLAIMS ALL REPRESENTATIONS AND WARRANTIES, EXPRESSED AND IMPLIED**, including the implied warranties of merchantability and fitness for a particular purpose.

Parks Projects (Page 2)
P01 – Frontier Park – North Field Improvements

Street & Traffic Projects (Page 3):
S01 – Coleman Street (Prosper Trail – Preston Road)
S02 – Mahard Parkway (north of US 380)
S03 – Richland Boulevard & Lovers Lane
S04 – West Prosper Road Improvements
S05 – US 380 (Lovers Lane – Custer Road)
S06 – US 380 (Denton County Line – Lovers Lane)

S07 – Frontier Parkway (DNT – Preston Road)
S08 – First Street (DNT – Coleman Street)
S09 – Prosper Trail (Kroger – Coit Road)
S10 – Prosper Trail (Coit Road – Custer Road)
S11 – First Street (Townlake Blvd - Custer Road)
S12 – Fishtrap (Teel Road – DNT)
S13 – Church Street (First Street – 8th Street)
S14 – Old Town Streets 2015
S15 – Decorative Monument Signs
S16 – First and DNT Traffic Signal

Water & Wastewater Projects (Page 8):
W01 – Rutherford Branch Sanitary Sewer Interceptor
W02 – 42" Lower Pressure Plane at Lovers Lane
W03 – Prosper Trail Elevated Storage Tank

Facility Projects (Page 9):
F01 – Windsong Ranch Fire Station
F02 – Town Hall / Multi-Purpose Facility

Drainage Projects (Page 10):
D01 – Church and Parvin Drainage Improvements
D02 – Hawk Ridge Drainage Improvements

PARKS

P01	Frontier Park – North Field Improvements		
<u>Project Scope:</u>	Construct three new all-weather youth baseball/softball fields and two all-weather multi-purpose fields. Also includes the construction of additional parking lots, bridge over pond with trails and park accoutrements.		
<u>Construction Start Date:</u>	Fall 2016 (estimated)	<u>Engineer:</u>	Dunaway Associates
<u>Construction End Date:</u>	Fall 2017 (estimated)	<u>Contractor:</u>	Dean Construction
<u>Current Phase:</u>	Design 20% Complete	<u>Est. Professional Cost:</u>	\$930,000
		<u>Est. Construction Cost:</u>	\$9,521,225
		<u>Total Project Cost:</u>	\$10,451,225
<u>Status Update:</u>	Staff continues coordinating with designers on proposed improvements. At a special called Council meeting on May 31, 2016, Council approved the expansion of the northwest and southwest youth ballfields from 225' outfields, to 275' outfields. The southwest ballfield center field will be extended further and both fields will have 10'-12' high chain link outfield fencing. The cost for these additions is estimated to not exceed \$700,000. The major components of the project are anticipated to be substantially complete for Town's Fall 2017 sports leagues.		

STREETS & TRAFFIC

S01 Coleman Street (Prosper Trail – Preston Road)	
<u>Project Scope:</u>	Construct two lanes of an ultimate 4-lane divided roadway from Prosper Trail to Preston Road. Project includes concrete pavement, underground drainage, a traffic signal at Prosper Trail, and a segment of 16-inch water line. The project is divided into two phases: Phase 1 includes work from Prosper Trail to PHS and Phase 2 includes work from PHS to Preston Road.
<u>Construction Start Date:</u>	Phase 1: March 2015 Phase 2: December 2015
<u>Construction End Date:</u>	Phase 1: September 2015 Phase 2: June 2016
<u>Current Phase:</u>	Phase 1: Construction Complete Phase 2: Construction Complete
<u>Status Update:</u>	Sub-contractor directed to finalize erosion control prior to final acceptance.
<u>Engineer:</u>	Kimley-Horn and Associates, Inc.
<u>Contractor:</u>	Phase 1: Tiseo Paving Co. Phase 2: Tiseo Paving Co.
<u>Total Project Cost:</u>	\$4,400,000 (Collin County Participation \$1,412,500)
S02 Mahard Parkway (north of US 380)	
<u>Project Scope:</u>	Developer project. Construct a new minor arterial roadway to be known as Mahard Parkway north of US 380 to serve new development.
<u>Construction Start Date:</u>	September 2015
<u>Construction End Date:</u>	Summer 2016
<u>Current Phase:</u>	Construction 60% Complete
<u>Status Update:</u>	Grading work and utility construction 99% complete. Crews prepping for stabilization. Construction is anticipated to be complete in Summer 2016.
<u>Engineer:</u>	Sanchez & Associates, LLC
<u>Contractor:</u>	Pavecon Ltd.
<u>Estimated Cost:</u>	TBD (Town participation through tax rebates)
S03 Richland Boulevard & Lovers Lane (Gates of Prosper)	
<u>Project Scope:</u>	Developer project. Construct 4-lane minor arterial roadways for Richland Boulevard (Preston Road – Lovers Lane) and Lovers Lane (US 380 – Preston Road) to serve the Gates of Prosper development at the northeast corner of US 380 & Preston Road.
<u>Construction Start Date:</u>	October 2015
<u>Construction End Date:</u>	October 2016 (estimated)
<u>Current Phase:</u>	Construction 35% Complete
<u>Status Update:</u>	Weather permitting, earthwork of the retail development site continues. Structure crews working on headwall at pond. Additional drainage pipe delivered. Plans for the portion of the 42" Lower Pressure Plane water line under Lovers Lane are scheduled to advertise June 29.
<u>Engineer:</u>	Kimley-Horn & Associates, Inc.
<u>Contractor:</u>	Mario Sinacola & Sons, Inc.
<u>Estimated Cost:</u>	\$2,900,000 (Town participation through tax rebates)

S04	West Prosper Road Improvements		
<u>Project Scope:</u>	Construct four-lane (ultimate six-lane) concrete curb & gutter roadway on Gee Road from US 380 to 800 feet north. Construct two-lane (ultimate six-lane) concrete curb & gutter roadways on Gee Road from 800 feet north of US 380 to Fishtrap Road, Fishtrap Road from Gee Road to FM 1385, and Teel Parkway from US 380 to Fishtrap Road. Construct two-lane (ultimate four-lane) concrete curb & gutter roadway on Fishtrap Road from Gee Road to Teel Parkway. Construct asphalt road improvements on FM 1385 at Fishtrap Road.		
<u>Construction Start Date:</u>	October 2015	<u>Engineer:</u>	Spiars Engineering, Inc.
<u>Construction End Date:</u>	TBD	<u>Contractor:</u>	Mario Sinacola & Sons, Inc.
<u>Current Phase:</u>	Construction 55% Complete		<u>Total Project Cost:</u> \$12.5 Million (Town Participation \$4.2 Million)
<u>Status Update:</u>	Structure crews nearing completion of large box culvert on Teel Parkway. Main line concrete paving completed on Gee Road and Fishtrap. Crews working on setting up decal lanes to pour during the week of June 27, 2016. Utility crews expected to arrive July 5 th , 2016 to begin installation of drainage improvements on Teel Parkway Staff reiterated to contractor the need to establish a safe roadway on Teel for motorists. Current work on Gee, Fishtrap, and Teel is anticipated to be complete in 3 rd Quarter 2016. Town staff is coordinating with TxDOT regarding the approval process for the realignment of FM 1385 at Fishtrap Road and approval of \$4 million in Regional Toll Revenue financing for this project.		
S05	US 380 (Lovers Lane – Custer Road)		
<u>Project Scope:</u>	TxDOT project. Improve four-lane undivided rural roadway to six-lane divided suburban roadway between Lovers Lane and Custer Road.		
<u>Construction Start Date:</u>	September 2014	<u>Engineer:</u>	TxDOT In-House
<u>Construction End Date:</u>	3 rd Quarter 2016 (estimated)	<u>Contractor:</u>	Mario Sinacola & Sons, Inc.
<u>Current Phase:</u>	Construction 99% Complete		<u>Total Project Cost:</u> \$23 Million (Town Participation \$0)
<u>Status Update:</u>	Continuing cleanup of parkways prior to Final acceptance. Final asphalt, pavement markings, hydromulch and sod scheduled for final completion June 26 through July 6, 2016. Motorists should anticipate minor delays when traveling through the area during these times. TxDOT Project Tracker: http://apps.dot.state.tx.us/apps-cq/project_tracker/		
S06	US 380 (Denton County Line – Lovers Lane)		
<u>Project Scope:</u>	TxDOT project. Improve four-lane undivided rural roadway to a six-lane suburban freeway with frontage roads in each direction between the Denton County Line and Lovers Lane. Through traffic on US 380 will bypass the SH 289 and Dallas Parkway intersections when completed.		
<u>Construction Start Date:</u>	January 2016	<u>Engineer:</u>	TxDOT In-House
<u>Construction End Date:</u>	3 rd Quarter 2018 (estimated)	<u>Contractor:</u>	Mario Sinacola & Sons, Inc.
<u>Current Phase:</u>	Construction 9% Complete		<u>Total Project Cost:</u> \$71 Million (Town Participation \$0)
<u>Status Update:</u>	Imported select fill being placed while retaining wall and bridge construction continues at BNSF overpass. Utility crews continue to install drainage improvements between BNSF and Legacy. Crews continue to work on subgrade for east bound frontage road between BNSF and Preston. Work also continues on southbound Preston frontage road, south side of US380. The entire project is expected to take 24-30 months to complete. TxDOT Project Tracker: http://apps.dot.state.tx.us/apps-cq/project_tracker/		

S07	Frontier Parkway (DNT – Preston Road)			
<u>Project Scope:</u>	Collin County project. Improve two-lane rural roadway to a four-lane (ultimate six-lane) divided suburban arterial between the Dallas North Tollway and Preston Road, including an overpass over the BNSF Railroad. A two-lane access road will be provided to the north of the overpass to provide access to properties in Celina.			
<u>Construction Start Date:</u>	TBD	<u>Engineer:</u>	Birkhoff Hendricks & Carter, LLP	
<u>Construction End Date:</u>	TBD	<u>Contractor:</u>	TBD	
<u>Current Phase:</u>	Planning	<u>Total Project Cost:</u>	\$16 Million (Town Participation \$3.65 Million)	
<u>Status Update:</u>	The Town of Prosper and the City of Celina both approved Resolutions supporting the project on January 12, 2016. Collin County will manage the design and construction of the project. A timeline for construction has not yet been determined.			
S08	First Street (DNT – Coleman Street)			
<u>Project Scope:</u>	Improve two-lane rural roadway to a four-lane divided suburban arterial between the Dallas North Tollway and Coleman Street. Project includes concrete curb and gutter roadway, underground drainage improvements, twelve inch water line, and median lighting.			
<u>Construction Start Date:</u>	TBD	<u>Engineer:</u>	Graham Associates, Inc.	
<u>Construction End Date:</u>	TBD	<u>Contractor:</u>	TBD	
<u>Current Phase:</u>	Design 60% complete	<u>Est. Professional Cost:</u>	\$550,000	
		<u>Est. Construction Cost:</u>	\$7,650,000	
		<u>Total Project Cost:</u>	\$8,200,000	
<u>Status Update:</u>	Staff received 60% submittal and review with Graham Associates February 17, 2016. Staff redirecting Engineer to center proposed roadway alignment on existing property lines between BNSF and Coleman Street. A timeline for construction to be determined once funding for construction is allocated. Staff coordinating with franchise utilities within the area.			
S09	Prosper Trail (Kroger - Coit Road)			
<u>Project Scope:</u>	Improve two-lane rural roadway to a four-lane divided suburban arterial from 1000' east of Preston Road to Coit Road as well as the Coit and Prosper Trail intersection. Project includes concrete curb and gutter roadway, underground drainage improvements, and median lighting.			
<u>Construction Start Date:</u>	TBD	<u>Engineer:</u>	Graham Associates, Inc.	
<u>Construction End Date:</u>	TBD	<u>Contractor:</u>	TBD	
<u>Current Phase:</u>	Design 70% complete	<u>Est. Professional Cost:</u>	\$305,000	
		<u>Est. Construction Cost:</u>	\$3,975,000	
		<u>Total Project Cost:</u>	\$4,280,000	
<u>Status Update:</u>	A timeline for construction to be determined once funding for construction is allocated. Staff considering options for separating design of Coit and Prosper Trail intersection to expedite construction.			
S10	Prosper Trail (Coit Road – Custer Road)			
<u>Project Scope:</u>	Resurface existing two lane asphalt road from the Coit Road intersection to the Custer Road intersection.			
<u>Construction Start Date:</u>	July 2016 (estimated)	<u>Engineer:</u>	In House	
<u>Construction End Date:</u>	August 2016 (estimated)	<u>Contractor:</u>	TBD	
<u>Current Phase:</u>	Pre-Construction	<u>Est. Construction Cost:</u>	\$347,768	
<u>Status Update:</u>	Bids received May 12, 2016. Council awarded contract to SPI Asphalt International at June 14, 2016, meeting. Contractor preparing to mobilize to begin work.			

S11	First Street (Townlake Boulevard – Custer Road)		
	<u>Project Scope:</u>	Resurface existing two lane asphalt road from Townlake intersection to the Custer Road intersection	
	<u>Construction Start Date:</u>	July 2016 (estimated)	<u>Engineer:</u> In House
	<u>Construction End Date:</u>	August 2016 (estimated)	<u>Contractor:</u> TBD
	<u>Current Phase:</u>	Pre-Construction	<u>Est. Construction Cost:</u> \$670,000
	<u>Status Update:</u>	Council awarded contract to Pavecon Public Works LP at the April 26, 2016, Town Council meeting. Work is scheduled to begin the week of July 11, 2016.	
S12	Fishtrap Road (Artesia – Dallas Parkway)		
	<u>Project Scope:</u>	Resurface existing two lane asphalt road from Artesia to the Dallas Parkway	
	<u>Construction Start Date:</u>	June 2016	<u>Engineer:</u> In House
	<u>Construction End Date:</u>	July 2016	<u>Contractor:</u> TBD
	<u>Current Phase:</u>	35% Complete	<u>Est. Construction Cost:</u> \$1,320,000
	<u>Status Update:</u>	Construction crews have stabilized approximately 60% of roadway. Motorists are reminded roadway is one way eastbound until work is completed.	
S13	Church Street (First Street – PISD)		
	<u>Project Scope:</u>	Reconstruction of existing two lane asphalt road to a concrete roadway without curb and gutter.	
	<u>Construction Start Date:</u>	Summer 2016	<u>Engineer:</u> In House
	<u>Construction End Date:</u>	Fall 2016	<u>Contractor:</u> TBD
	<u>Current Phase:</u>	Bidding	<u>Est. Construction Cost:</u> \$850,000
	<u>Status Update:</u>	Staff has begun advertising construction package. Bid opening scheduled for July 19, 2016.	
S14	Old Town Streets 2015		
	<u>Project Scope:</u>	Reconstruction of existing two lane asphalt roads to a concrete roadway without curb and gutter (Broadway, Fifth, McKinley)	
	<u>Construction Start Date:</u>	Late Fall 2016	<u>Engineer:</u> TBD
	<u>Construction End Date:</u>	Spring 2017	<u>Contractor:</u> TBD
	<u>Current Phase:</u>	Pre-Design	<u>Est. Construction Cost:</u> \$1,044,000
	<u>Status Update:</u>	Staff working on design options and selection of engineer.	
S15	Decorative Monument Signs		
	<u>Project Scope:</u>	Construct eight decorative stone and steel signs at La Cima and First (3 EA), First and Coit (2 EA), and Coit and Richland (3 EA) intersections.	
	<u>Construction Start Date:</u>	March 2016	<u>Engineer:</u> In House
	<u>Construction End Date:</u>	Summer 2016	<u>Contractor:</u> Starlight Signs
	<u>Current Phase:</u>	Construction 50% Complete	<u>Total Project Cost:</u> \$130,000
	<u>Status Update:</u>	Crews have resumed construction of stone signage at First Street and Coit Road.	

S16

First Street and Dallas Parkway Traffic Signal

<u>Project Scope:</u>	Construct span wire traffic signal at First Street and Dallas Parkway intersection.		
<u>Construction Start Date:</u>	July 2016	<u>Engineer:</u>	Lee Engineering
<u>Construction End Date:</u>	August 2016	<u>Contractor:</u>	TBD
<u>Current Phase:</u>	Bid Advertisement	<u>Total Project Cost:</u>	\$220,000
<u>Status Update:</u>	Bid opening scheduled for June 30, 2016.		

WATER & WASTEWATER

W01	Rutherford Branch Sewer Interceptor		
<u>Project Scope:</u>		Developer project. Construct approximately 2 miles of variable diameter (24-inch to 8-inch) sanitary sewer main along Rutherford Branch to provide sanitary sewer service to a large area of southeast Prosper, between Coit and Custer, south of Richland Boulevard.	
<u>Construction Start Date:</u>	June 2016	<u>Engineer:</u>	Corwin Engineering
<u>Construction End Date:</u>	October 2016	<u>Contractor:</u>	Mario Sinacola & Sons
<u>Current Phase:</u>	10% Complete	<u>Estimated Cost:</u>	\$1,080,000
<u>Status Update:</u>	Contractor has begun installation of sewer line. Difficult soil conditions have resulted in diminished productivity.		
W02	Lovers Lane Segment – 42" Lower Pressure Plane Water (Gates of Prosper)		
<u>Project Scope:</u>		Construct 2400 LF segment of 42" water line under Lovers Lane from Richland Boulevard to Preston Road prior to Developer constructing roadway.	
<u>Construction Start Date:</u>	July 2016 (estimated)	<u>Engineer:</u>	Freese & Nichols, Inc.
<u>Construction End Date:</u>	October 2016 (estimated)	<u>Contractor:</u>	TBD
<u>Current Phase:</u>	Design Complete	<u>Estimated Cost:</u>	\$1,340,000
<u>Status Update:</u>	Staff anticipates bidding June 29, 2016.		
W03	Prosper Trail Elevated Storage Tank		
<u>Project Scope:</u>		Construct a 2 million gallon elevated storage tank (water tower) on the north side of Prosper Trail, midway between Preston Road and Coit Road.	
<u>Construction Start Date:</u>	January 2016	<u>Engineer:</u>	Brown & Gay Engineers
<u>Construction End Date:</u>	June 2017 (estimated)	<u>Contractor:</u>	Landmark Structures
<u>Current Phase:</u>	Construction 45% Complete	<u>Est. Professional Cost:</u>	\$517,300
		<u>Est. Construction Cost:</u>	\$4,403,300
		<u>Total Project Cost:</u>	\$4,920,600
<u>Status Update:</u>	Crews have completed dome floor. Steel for tank construction being fabricated, delivery anticipated July 6 & 7. Internal scaffolding and ladder safety measures 90% complete. All work is anticipated to be complete in June 2017.		

FACILITIES

F01	Windsong Ranch Fire Station		
	<u>Project Scope:</u>	Construct a second fire station to be located on Teel Parkway between US 380 and Fishtrap Road.	
	<u>Construction Start Date:</u>	August 2015	<u>Architect:</u> Wington Hooker Jeffry Architects
	<u>Construction End Date:</u>	August 2016 (estimated)	<u>Contractor:</u> Pogue Construction Co., LLC
	<u>Current Phase:</u>	Construction 67% Complete	<u>Total Project Cost:</u> \$7,500,000
	<u>Status Update:</u>	Masonry crews continue to work on exterior walls, approximately 70% complete. Roof construction 70% complete.	
F02	Town Hall / Multi-Purpose Facility		
	<u>Project Scope:</u>	Construct a Town Hall / Multi-Purpose Facility to serve the Town's increasing needs, including administrative offices, council chambers, municipal court, library, multi-purpose rooms, and other functions. Estimated cost includes construction services, equipment, and furniture.	
	<u>Construction Start Date:</u>	3 rd Quarter 2016 (estimated)	<u>Architect (Facility):</u> Randall Scott Architects
	<u>Construction End Date:</u>	4 th Quarter 2017 (estimated)	<u>Contractor (Facility):</u> Pogue Construction Co., LLC
	<u>Current Phase:</u>	Design 40% Complete	<u>Est. Professional Cost:</u> \$1,550,000
			<u>Est. Construction Cost:</u> \$20,175,000
			<u>Total Project Cost:</u> \$21,725,000
	<u>Status Update:</u>	Town Council continues to provide direction regarding scope and timeline of the facility with a move-in goal of 4 th Quarter 2017. Council authorized the use of Pogue Construction for Construction Manager At-Risk services on September 8, 2015. 100% Design Development plans received May 5, 2016, which equals to approximate 40% construction plans.	
F02	Town Hall / Infrastructure		
	<u>Project Scope:</u>	Reconstruction of Main Street (First Street to Broadway) to curb and guttered concrete roadway. Project also constructs additional street within alley easement south of Broadway to Crockett. In addition to pavement, project includes water, sewer, and drainage improvements for Town Hall, as well as, lighting and landscaping improvements for Main Street.	
	<u>Construction Start Date:</u>	3 rd Quarter 2016 (estimated)	<u>Engineer (Infrastructure):</u> Teague Nall and Perkins, Inc.
	<u>Construction End Date:</u>	3 rd Quarter 2016 (estimated)	<u>Contractor (Infrastructure):</u> TBD
	<u>Current Phase:</u>	Design 99% Complete	<u>Est. Professional Cost:</u> \$184,000
			<u>Est. Construction Cost:</u> \$1,091,000
			<u>Total Project Cost:</u> \$1,275,000
	<u>Status Update:</u>	Final plans expected to be delivered July 7, 2016. Discussions with owner of needed ROW continue, AT&T has begun preliminary work associated with utility relocations. Oncor expected to begin in mid-July 2016	

DRAINAGE

Church and Parvin Drainage Improvements			
<u>Project Scope:</u>	Design of underground storm sewer currently flowing through an unimproved alley and across residential lots east between Church Street and Parvin Street, north of Broadway and south of Seventh Street.		
<u>Construction Start Date:</u>	TBD	<u>Engineer:</u>	Wier & Associates Inc.
<u>Construction End Date:</u>	TBD	<u>Contractor:</u>	TBD
<u>Current Phase:</u>	Design	<u>Est. Professional Cost:</u>	\$109,500
		<u>Est. Construction Cost:</u>	\$390,500
		<u>Total Project Cost:</u>	\$500,000
<u>Status Update:</u>	Design contract approved by Town Council at November 10, 2015 meeting. Engineer working on preliminary models based on data gathered in late-May and early June.		
D02 Hawk Ridge Drainage Improvements			
<u>Project Scope:</u>	Construction of retaining walls and 200 feet of concrete flume between Hawk Ridge and Seventh Street properties.		
<u>Construction Start Date:</u>	March 2016	<u>Engineer:</u>	Wier & Associates Inc.
<u>Construction End Date:</u>	June 2016 (estimated)	<u>Contractor:</u>	Gilco Construction
<u>Current Phase:</u>	Construction 30% Complete	<u>Total Project Cost:</u>	\$120,000
<u>Status Update:</u>	Crews continue to excavate and form pilot channel within culvert. Staff continues to work with Oncor on stabilization of power pole.		
